
Madison County Landfill, Canastota, New York: revised sizing

What the landfill gas could power today and at the County's target gas quality, how much land it would take, and what it could earn each year.

0.6 → 1.0	1	6 ac	87k
MW, TODAY → TARGET	COMPUTE MODULE	LAND NEEDED	MMBTU / YR AT TARGET

TODAY, PER YEAR	AT TARGET, PER YEAR	WHAT BETTER GAS ADDS, PER YEAR
$6k to $64k	$6k to $187k	up to $122k

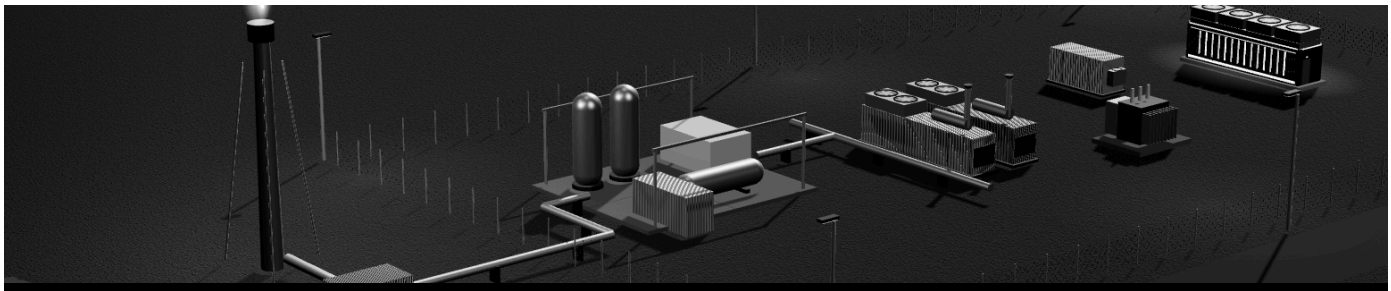

THE SITE AT TARGET IN OUR LIVE 3D MODEL ACCRETIONCOMPUTE.COM/SITE-MODEL?SRC=LFG&FLOW=360&CH4=48

THE MATH

	TODAY	AT TARGET
Landfill gas collected	350 scfm	360 scfm
Methane content	30%	48%
Power at 11,000 Btu/kWh	about 0.6 MW	about 1.0 MW
Compute (after cooling and losses)	about 0.5 MW	about 0.8 MW
Gas engines (incl. one spare)	2 at 1.6 MW	2 at 1.6 MW
Land (5 ac + 1.2 ac per MW)	about 6 acres	about 6 acres
Gas bought a year (95% run)	53k MMBtu	87k MMBtu
Gas price, per MMBtu	up to $1.00	up to $2.00
Gas payment, per year	up to $53k	up to $175k
Land, $1,000–2,000 per acre	$6k to $11k	$6k to $12k
Total to the County, per year	**$6k to $64k**	**$6k to $187k**

Landfill gas: about 1,012 Btu per cubic foot of methane. Prices in US dollars.

WHAT IT WOULD LOOK LIKE

- Gas engines, a battery to smooth the load, and factory-built compute modules leased to an AI company, on a fenced parcel near the gas.
- The County keeps running the wellfield and delivers gas to our meter. Gas at the target quality is paid twice the price.
- Runs on its own engines. If the earlier project's grid connection is still in place, it could serve as backup.
- We build and run the site; the County puts in no capital. Engine heat is available for the ARE Park.

TO FIRM UP THE NUMBERS

- 12 to 24 months of flow, methane and oxygen readings
- Equipment still in place from the earlier project
- Whether the earlier grid connection is still in place, and its size
- ARE Park utilities and acres; gas quality (siloxanes, H2S)

Source: Madison County gas readings shared in November 2026: today about 350 scfm at 30% methane; the County's target is 350 to 375 scfm at 45 to 50% methane (the target column uses 360 scfm at 48%). These are estimates from the County's readings, not an offer: no cost and no obligation. Twelve to 24 months of readings will firm them up; the real price and terms are set in the gas and land agreements.
