
# New Boston Landfill, New Boston, Bowie County, Texas: site sizing

What the gas the site now flares could power, how much land it would take, and what it could earn each year.

| 2.3 MW | 2 | 8 ac | 210k |
|---|---|---|---|
| POWER FROM THE GAS | COMPUTE MODULES | LAND NEEDED | MMBTU BOUGHT / YR |

| GAS SALE, PER YEAR | LAND LEASE, PER YEAR | TOTAL TO THE OWNER, PER YEAR |
|---|---|---|
| up to $631k | $8k to $16k | $8k to $647k |

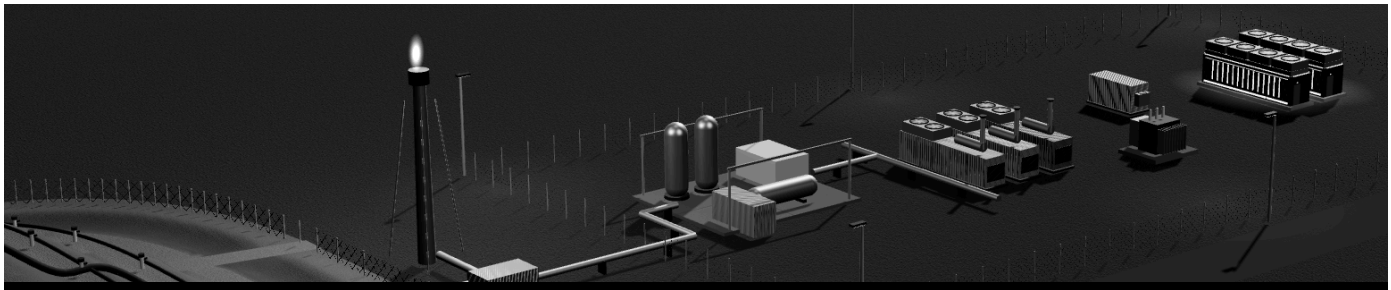

YOUR SITE IN OUR LIVE 3D MODEL — ACCRETIONCOMPUTE.COM/SITE-MODEL?SRC=LFG&FLOW=863&CH4=48

## THE MATH

| | |
|---|---|
| Landfill gas collected and flared (2022) | 863 scfm |
| Methane content (2022) | 48.2% |
| Energy in the gas | 25.3 MMBtu per hour |
| Power at a heat rate of 11,000 Btu/kWh | about 2.3 MW |
| Compute (power less cooling and losses, /1.2) | about 1.9 MW |
| Compute modules (about 1 MW each) | 2 |
| Gas engines (running plus one spare) | 3 at 1.6 MW |
| Land: 5 acres plus 1.2 acres per MW | about 8 acres |
| Gas bought per year (95% run time) | 210k MMBtu |
| Gas payment, up to $3.00/MMBtu | up to $631k |
| Land lease at $1,000 to $2,000 per acre per year | $8k to $16k |

Landfill gas: about 1,012 Btu per cubic foot of methane. Prices in US dollars; the price band is the one shown on our Site model page.

## WHAT IT WOULD LOOK LIKE

- Our own gas engines on a fenced parcel near the gas, a battery to smooth the load, and factory-built compute modules leased to an AI company.
- No grid connection and no export: all of the power is used on site.
- We build and run the site. The owner puts in no capital.
- Multi-year gas and land agreements, matched to the tenant's lease, at a fixed price.

## WORTH CHECKING

- The site's summer 2025 newsletter says new horizontal gas wells have significantly increased gas flow, so today's figure is likely higher
- Whether the gas is set aside for another use
- Space for a fenced parcel near the flare
- Gas quality (siloxanes, H2S) for engines
- Bowie County approvals for the parcel

**Source:** EPA Landfill Methane Outreach Program (LMOP) database, September 2024 release (2022 data): about 1.24 million cubic feet a day (863 scfm) flared at 48.2% methane; open, closure year 2059; no energy project on record. This is an estimate from public data, not an offer: no cost and no obligation. The real price and terms are set in the gas and land agreements after a site review.
